

21-218 Francis Marion Hotel

387 King Street Charleston, South Carolina 29403



Date Mon 09/12/2022

Job # 21-218

Prepared By Jamie Donaldson

Weather



<div>6:00 AM</div> <div>78°</div> <div>Humid and Partly Cloudy</div> <div>Wind: 3 MPH Precipitation: .02" Humidity: 87%</div>	<div>12:00 PM</div> <div>84°</div> <div>Humid and Mostly Cloudy</div> <div>Wind: 7 MPH Precipitation: .03" Humidity: 76%</div>	<div>4:00 PM</div> <div>82°</div> <div>Humid and Mostly Cloudy</div> <div>Wind: 12 MPH Precipitation: .05" Humidity: 77%</div>
---	--	--










Work Logs






Name	Description	Quantity	Total Hours
Jamie Donaldson	<p>One crew continued removing and replacing windows sealants on Calhoun rise #4. The other crew began removing one window in unit 1203. The one window was removed and it was discovered that the wooden frame is the old components of the last window and a majority of the wood components are rotted. The windows sill ended up being rotted on the ends so it will need to be replaced.</p> <p>Structural bonding pins were installed and the crew began installing new mortar along the jambs for installing the new window properly. Randall with CQS brought a new cable out for rise #3. The decision to complete an additional window per OCO #7 or not, was discussed with the Dopp's. A decision has not been made yet on whether to do a second window in this manner or not.</p> <p>Jamie Donaldson 09/13/22 10:04AM</p>	4	28
Total		4	28

Work Log Photos

Jamie Donaldson: | QTY: 4 | HRS: 7.0

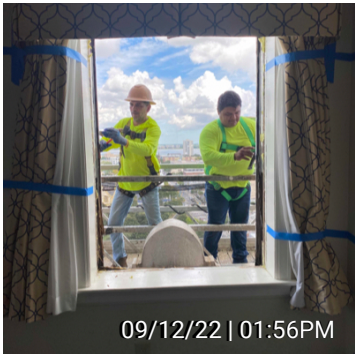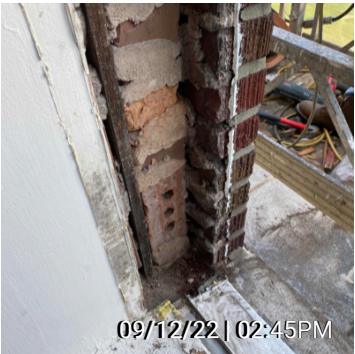

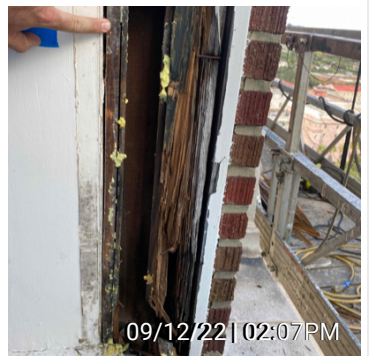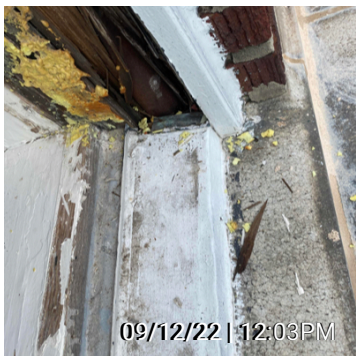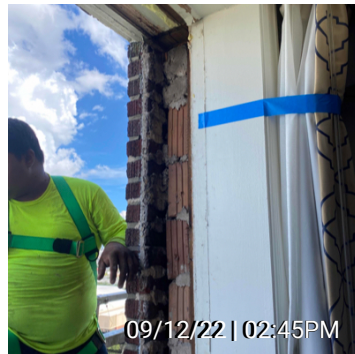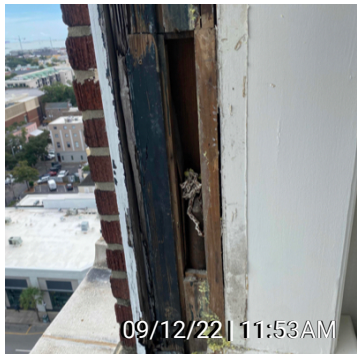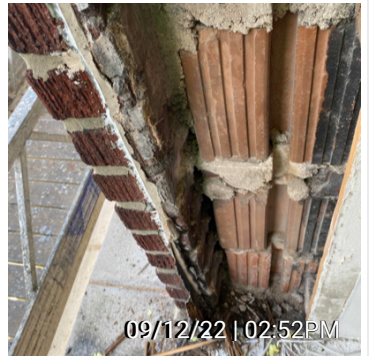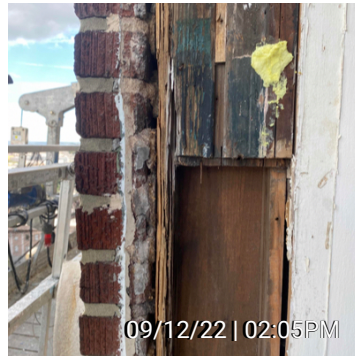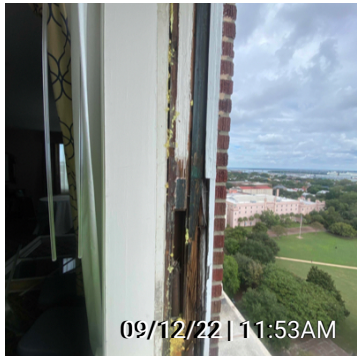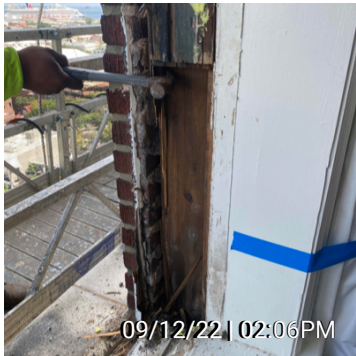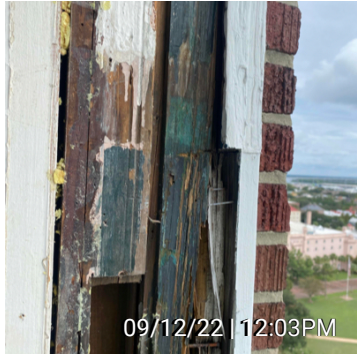

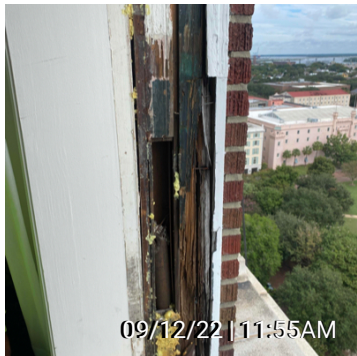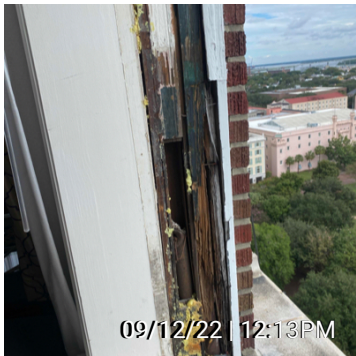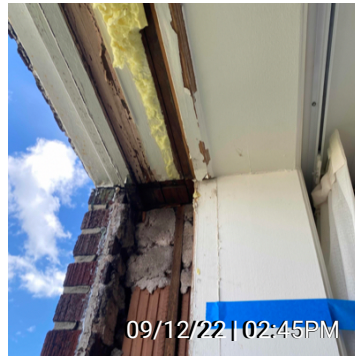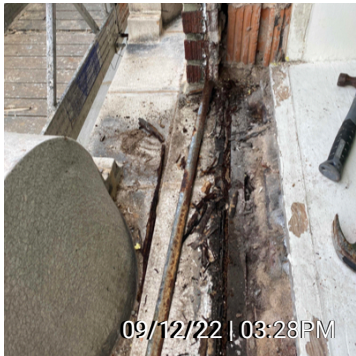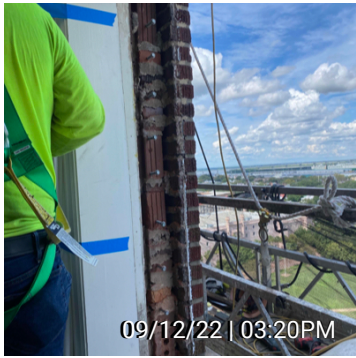

Survey

Questions

N/A No Yes Description

1. Materials forecasted for upcoming week?

☐ ☐ ☒

2. Any accidents on site today?

☐ ☒ ☐

3. Was the Covid-19 protocol discussed? ☐ ☒ ☐

4. Any schedule delays occur? ☐ ☒ ☐

5. Any weather delays occur? ☐ ☒ ☐

6. Any Covid-19 related delays? ☐ ☒ ☐

7. Any visitors on site? ☐ ☐ ☒ **Randall CQS**
Jamie Donaldson | 09/13/22 | 10:05AM

8. Any areas that can't be worked on? ☐ ☐ ☒ **The additional window per OCO #7**
Jamie Donaldson | 09/13/22 | 10:05AM

9. Competent Person/Equipment Checklist? ☐ ☐ ☒

10. Any equipment rented on site? ☐ ☐ ☒

11. Were temporary toilets and wash stations serviced? ☐ ☒ ☐



I, Jamie Donaldson, have reviewed and completed this report.

Jamie Donaldson | 09/13/22 | 10:05AM
